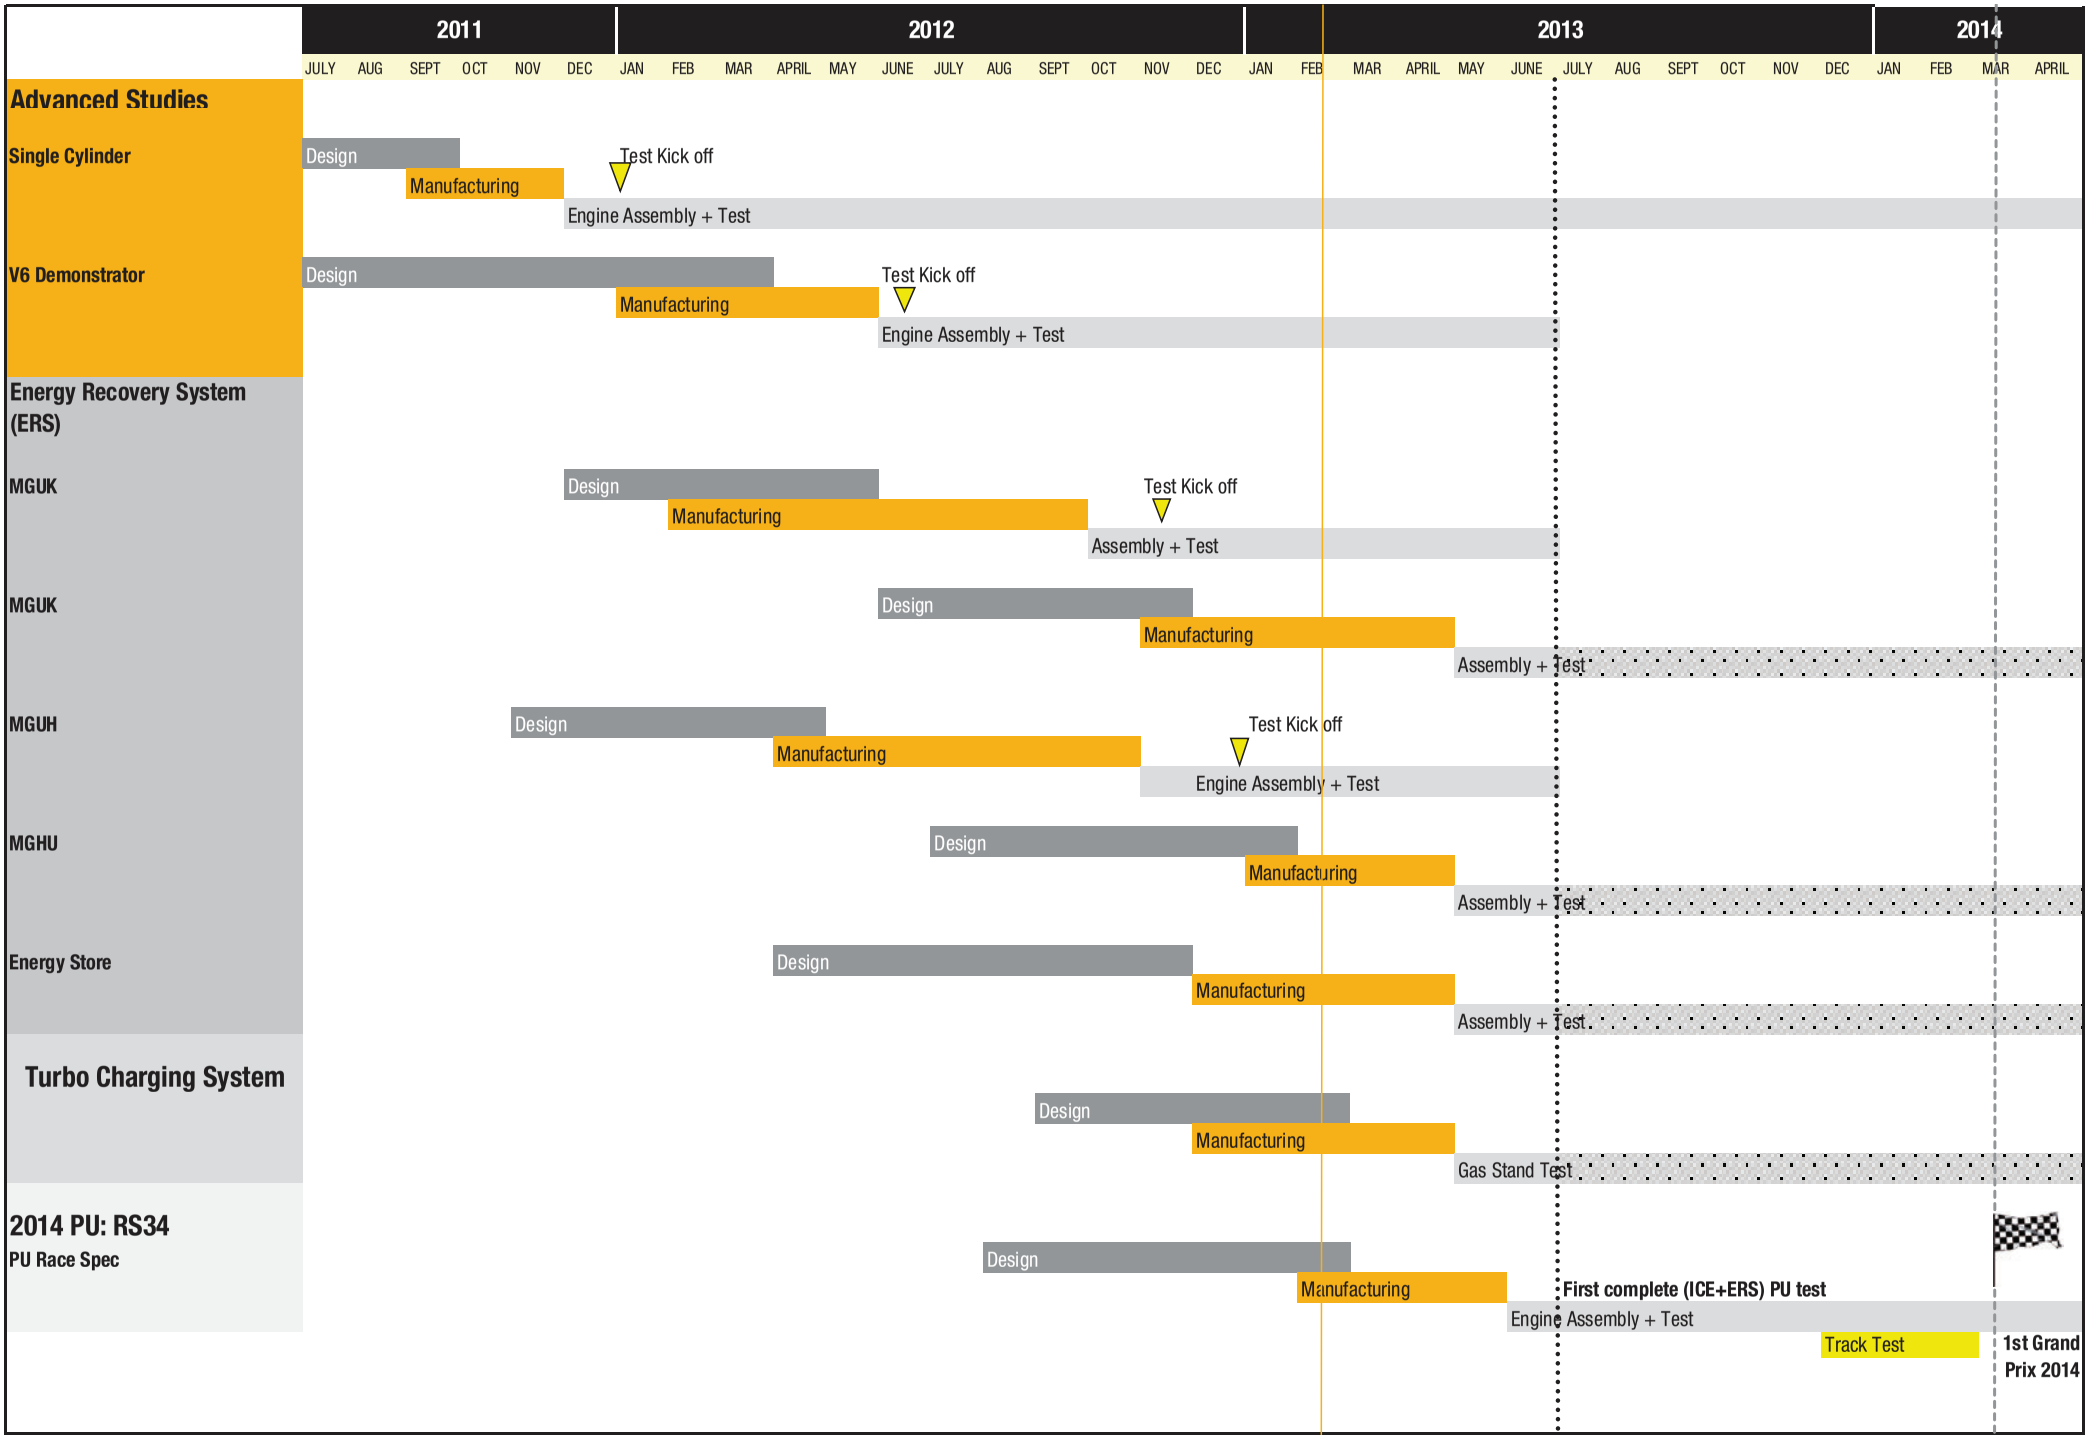
2011
2012
2013
2014
JULY AUG SEPT OCT NOV DEC JAN FEB MAR APRIL MAY JUNE JULY AUG SEPT OCT NOV DEC JAN FEB MAR APRIL MAY JUNE JULY AUG SEPT OCT NOV DEC JAN FEB MAR APRIL
Advanced Studies
Single Cylinder
Design
Manufacturing
Test Kick off
Engine Assembly + Test
V6 Demonstrator
Design
Manufacturing
Test Kick off
Engine Assembly + Test
Energy Recovery System (ERS)
MGUK
Design
Manufacturing
Test Kick off
Assembly + Test
MGUK
Design
Manufacturing
Assembly + Test
MGUH
Design
Manufacturing
Test Kick off
Engine Assembly + Test
MGHU
Design
Manufacturing
Assembly + Test
Energy Store
Design
Manufacturing
Assembly + Test
Turbo Charging System
Design
Manufacturing
Gas Stand Test
2014 PU: RS34
PU Race Spec
Design
Manufacturing
First complete (ICE+ERS) PU test
Engine Assembly + Test
Track Test
1st Grand Prix 2014
